


Activity ID	Activity Name	Orig. Dur.	Early Start	Early Finish	Total Float	2021												2022							
						Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar
Project: Attleboro Public Library -Update No. 1																									
WBS: MILESTONES / Key Events																									
M1000	Proposal Submitted to Owner	0	01-Sep-20 A																						
M1026	Building Permit Application	10	28-Sep-20 A	06-Oct-20 A																					
M1020	Owner Review / Notice to Proceed	6	01-Oct-20 A	02-Oct-20 A																					
M1029	Mobilize	0	12-Oct-20 A																						
M9120	Substantial Completion (July 31, 2021)	0		30-Jul-21*	1																				
M9130	Project Closeout (45 cal. days)	45	31-Jul-21	13-Sep-21	1																				
M9140	Project Complete	0		13-Sep-21*	1																				
WBS: PROCUREMENT																									
WBS: Critical Path Subcontractors																									
S1019	Award Critical Path Subcontractors	10	18-Sep-20 A	23-Sep-20 A																					
WBS: Subcontractors																									
S1029	Award Subcontractors	25	14-Oct-20 A	21-Oct-20 A																					
WBS: Masonry																									
S1025	Submit/Review/Approve for Mock Up - Masonry	40	16-Oct-20 A	03-Nov-20	2																				
S2590	Approve Mock Up- Masonry	4	19-Nov-20	24-Nov-20	5																				
S2630	Deliver Material- Masonry	35	25-Nov-20	12-Jan-21	29																				
WBS: Metals																									
WBS: Copper Cleaning and Repairs																									
S1026	Submit/Review/Approve - Copper Restoration	30	27-Oct-20	07-Dec-20	89																				
WBS: Cast Iron																									
S3330	Cast Iron Existing Conditions Review	20	20-Nov-20	21-Dec-20	44																				
S2640	Submit/Review/Approve - Cast Iron	5	22-Dec-20	28-Dec-20	46																				
S3570	Cast Iron Restoration Mockup	10	29-Dec-20	12-Jan-21	45																				
S3550	Cast Iron Restoration Off-Site Mockup Approval	5	13-Jan-21	19-Jan-21	45																				
S3560	Cast Iron Restoration	60	20-Jan-21	13-Apr-21	45																				
WBS: Aluminum Ladders																									
S2650	Submit/Review/Approve - Aluminum Ladders	15	27-Oct-20	16-Nov-20	143																				
S2660	Fab & Deliver - Aluminum Ladders	30	17-Nov-20	28-Dec-20	143																				
WBS: Structure Supports for Roof Top Equipment																									
S2530	Submit/Review/Approve - Structural Steel	10	27-Oct-20	09-Nov-20	114																				
S2670	Fab & Deliver - Structural Steel	20	10-Nov-20	07-Dec-20	114																				
WBS: Wood, Plastics & Composites																									
S1036	Submit/Review/Approve/Deliver - Rough Carpentry	10	27-Oct-20	09-Nov-20	11																				
WBS: Thermal and Moisture Protection																									
WBS: Slate Shingles																									
S2680	Submit/Review/Approve - Slate Shingles	25	20-Oct-20 A	27-Oct-20	63																				
S2690	Procure - Slate Shingles	40	28-Oct-20	22-Dec-20	63																				
WBS: EPDM Roofing																									
S2700	Submit/Review/Approve - EPDM Roofing	10	15-Oct-20 A	27-Oct-20	10																				
S2710	Procure - EPDM Roofing	10	28-Oct-20	10-Nov-20	10																				
WBS: Thermoplastic Membrane Roofing																									
S2720	Submit/Review/Approve - Thermoplastic Membrane Roofing	10	15-Oct-20 A	27-Oct-20	10																				
S2730	Procure - Thermoplastic Membrane Roofing	10	28-Oct-20	10-Nov-20	10																				
WBS: Sheet Metal Flashing and Trim																									
S2740	Submit/Review/Approve - Sheet Metal Flashing and Trim	10	15-Oct-20 A	27-Oct-20	10																				
S2750	Procure - Sheet Metal Flashing and Trim	10	28-Oct-20	10-Nov-20	10																				
WBS: Roofing Specialities																									
		44	15-Oct-20 A	24-Nov-20	0																				

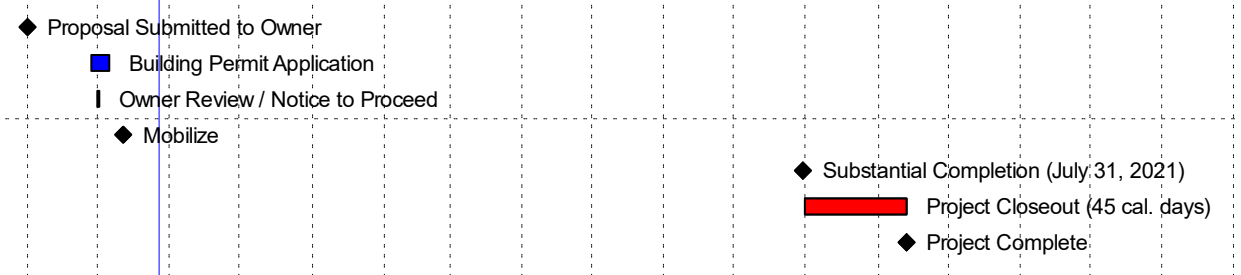

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

**Attleboro Public Library Building Envelop Repair
& Mechanical System Upgrade
Schedule Update No. 1**

Prepared by Turino Group, Inc.			
Date	Revision	Checked	Approved



Activity ID	Activity Name	Orig. Dur.	Early Start	Early Finish	Total Float	2021												2022							
						Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar
S2760	Submit/Review/Approve - Roofing Specialities	10	15-Oct-20 A	27-Oct-20	0																				
S2770	Procure - Roofing Specialities	20	28-Oct-20	24-Nov-20	0																				
WBS: Joint Sealants		44	15-Oct-20 A	24-Nov-20	147																				
S2780	Submit/Review/Approve - Exterior Joint Sealant	10	15-Oct-20 A	27-Oct-20	151																				
S2820	Submit/Review/Approve - Interior Joint Sealant	10	15-Oct-20 A	27-Oct-20	151																				
S2790	Joint Sealant Mockups -Exterior / Interior	10	28-Oct-20	10-Nov-20	147																				
S2800	Approve Joint Sealant Mockups - Exterior/ Interior	5	11-Nov-20	17-Nov-20	147																				
S2810	Procure Joint Sealants - Exterior/Interior	5	18-Nov-20	24-Nov-20	152																				
WBS: Doors & Windows		86	27-Oct-20	01-Mar-21	89																				
WBS: Skylights		66	27-Oct-20	01-Feb-21	109																				
S3350	Submit/Review/Approve Product Data- Skylights	15	27-Oct-20	16-Nov-20	111																				
S3370	Submit/Review/Approve Shop Drawings & Cals- Skylights	15	27-Oct-20	16-Nov-20	111																				
S3380	Submit/Review/Approve Samples -Skylights	15	27-Oct-20	16-Nov-20	111																				
S3390	Field Measurements -Skylights	5	17-Nov-20	23-Nov-20	107																				
S3360	Fab & Deliver - Skylights	50	24-Nov-20	01-Feb-21	111																				
WBS: Interior Aluminum Storm Windows		76	27-Oct-20	15-Feb-21	97																				
S3420	Submit/Review/Approve Shop Drawings - Interior Aluminum Storm Windows	20	27-Oct-20	23-Nov-20	98																				
S3430	Submit/Review/Approve Samples -Interior Aluminum Storm Windows	5	24-Nov-20	30-Nov-20	98																				
S3440	Field Measurements -Interior Aluminum Storm Windows	5	01-Dec-20	07-Dec-20	96																				
S3410	Fab & Deliver - InteriorAluminum Storm Windows	50	08-Dec-20	15-Feb-21	98																				
WBS: Glazing		80	27-Oct-20	19-Feb-21	93																				
S3460	Submit/Review/Approve Shop Drawings - Glazing	20	27-Oct-20	23-Nov-20	118																				
S3470	Submit/Review/Approve Samples -Glazing	5	24-Nov-20	30-Nov-20	118																				
S3480	Field Measurements -Glazing	5	04-Jan-21	08-Jan-21	94																				
S3450	Fab & Deliver - Glazing	30	11-Jan-21	19-Feb-21	94																				
WBS: Hollow Metal Door		86	27-Oct-20	01-Mar-21	37																				
S3520	Submit/Review/Approve Shop Drawings -Hollow Metal Door	20	27-Oct-20	23-Nov-20	37																				
S3530	Submit/Review/Approve Samples -Hollow Metal Door	15	24-Nov-20	14-Dec-20	37																				
S3540	Field Measurements -Hollow Metal Door	5	15-Dec-20	21-Dec-20	35																				
S3510	Fab & Deliver - Hollow Metal Door	50	22-Dec-20	01-Mar-21	37																				
WBS: Wood Window Restoration		15	18-Dec-20	11-Jan-21	0																				
S3490	Mockup - Wood Window Restoration	10	18-Dec-20	04-Jan-21	0																				
S3500	Approve Mockup -Wood Window Restoration	5	05-Jan-21	11-Jan-21	0																				
WBS: Finishes		155	09-Oct-20 A	04-May-21	44																				
S1090	Submit/Review/Approve/Deliver - Architectural Finishes	20	27-Oct-20	23-Nov-20	50																				
S2570	Submit/Review/Approve/Deliver - ACT	25	27-Oct-20	30-Nov-20	45																				
S2830	Submit/Review/Approve/Deliver - Gypsum Board	23	27-Oct-20	26-Nov-20	47																				
S2840	Submit/Review/Approve/Deliver - Plaster Patching	23	27-Oct-20	26-Nov-20	47																				
S2850	Submit/Review/Approve/Deliver - VCT Flooring	30	27-Oct-20	07-Dec-20	123																				
S2860	Submit/Review/Approve/Deliver - Carpeting & Adhesives	30	27-Oct-20	07-Dec-20	40																				
WBS: Painting		155	09-Oct-20 A	04-May-21	44																				
S2540	Submit/Review/Approve - Paint	20	09-Oct-20 A	05-Nov-20	20																				
WBS: Copper Restoration Paint		10	26-Feb-21	11-Mar-21	61																				
S287	Exterior Copper Restoration Paint Mockup	5	26-Feb-21	04-Mar-21	61																				
S356	Exterior Copper Restoration Paint Mockup Approval	5	05-Mar-21	11-Mar-21	61																				
WBS: Cast Iron Restoraton Paint		15	14-Apr-21	04-May-21	44																				
S346	Cast Iron Balconies & Light Posts Paint Mockup	5	14-Apr-21	20-Apr-21	44																				
S286	Cast Iron Balconies & Light Posts Paint Mockup Approval	5	21-Apr-21	27-Apr-21	44																				
S360	Paint Cast Iron Balconies & Light Posts	5	28-Apr-21	04-May-21	44																				

Data Date 27-Oct-20
 Run Date 12-Nov-20 11:50
 Print Date 12-Nov-20
 Page 2 of 6

- █ Remaining Level of Effort
- █ Actual Level of Effort
- █ Actual Work
- █ Remaining Work
- █ Critical Remaining Work
- ◆ Milestone

**Attleboro Public Library Building Envelop Repair
& Mechanical System Upgrade
Schedule Update No. 1**

Prepared by Turino Group, Inc.

Date	Revision	Checked	Approved



Activity ID	Activity Name	Orig. Dur.	Early Start	Early Finish	Total Float	2021												2022							
						Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar
A1330	Strip, Repair, & Re-Roof -Main Roof P2	20	08-Jan-21	04-Feb-21	106						Strip, Repair, & Re-Roof -Main Roof P2														
A1370	Install Skylights -Main Roof P2	10	05-Feb-21	18-Feb-21	106						Install Skylights -Main Roof P2														
A1990	Install Roof Ladders - P2	3	05-Feb-21	09-Feb-21	113						Install Roof Ladders - P2														
A2130	Install Roof Drainage Accessories -Exterior P2	3	05-Feb-21	09-Feb-21	107						Install Roof Drainage Accessories -Exterior P2														
A2160	Paint Roof Drainage Accessories -Exterior P2	3	10-Feb-21	12-Feb-21	110						Paint Roof Drainage Accessories -Exterior P2														
A1350	Reinstall Mechanical Equipment -Main Roof P2	10	12-Feb-21	25-Feb-21	104						Reinstall Mechanical Equipment -Main Roof P2														
A2190	Punchlist Roof -Exterior P2	3	19-Feb-21	23-Feb-21	106						Punchlist Roof -Exterior P2														
WBS: East Roof		88	23-Dec-20	27-Apr-21	61																				
A1380	Demo of Existing Slate Roofing -East Roof	5	23-Dec-20	30-Dec-20	61						Demo of Existing Slate Roofing -East Roof														
A1390	Installation of New Roofing -East Roof	10	31-Dec-20	14-Jan-21	61						Installation of New Roofing -East Roof														
A1400	Copper Restoration -East Roof	30	15-Jan-21	25-Feb-21	61						Copper Restoration -East Roof														
A2140	Install Roof Drainage Accessories -Exterior East Roof	3	10-Feb-21	12-Feb-21	107						Install Roof Drainage Accessories -Exterior East Roof														
A2170	Paint Roof Drainage Accessories -East Roof	3	15-Feb-21	17-Feb-21	107						Paint Roof Drainage Accessories -East Roof														
A2110	Paint Copper -East Roof	30	12-Mar-21	22-Apr-21	61						Paint Copper -East Roof														
A2200	Punchlist Roof -Exterior P1	3	23-Apr-21	27-Apr-21	61						Punchlist Roof -Exterior P1														
WBS: Masonry Restoration		133	20-Nov-20	01-Jun-21	37																				
A1790	Setup Scaffolding for Masonry Restoration	20	20-Nov-20	21-Dec-20	1						Setup Scaffolding for Masonry Restoration														
A1410	Masonry Restoration 1907	60	13-Jan-21	06-Apr-21	29						Masonry Restoration 1907														
A1420	Masonry Restoration 1992	30	02-Mar-21	12-Apr-21	37						Masonry Restoration 1992														
A2230	Punchlist Masonry Restoration 1907	30	07-Apr-21	18-May-21	29						Punchlist Masonry Restoration 1907														
A2220	Punchlist Masonry Restoration 1992	30	13-Apr-21	24-May-21	37						Punchlist Masonry Restoration 1992														
A1780	Remove Scaffolding 1907	5	19-May-21	25-May-21	29						Remove Scaffolding 1907														
A1980	Remove Scaffolding 1992	5	25-May-21	01-Jun-21	37						Remove Scaffolding 1992														
WBS: Cast Iron Restoration		159	27-Oct-20	11-Jun-21	29																				
A1950	Schedule / Make Safe Light Posts	12	27-Oct-20	11-Nov-20	1						Schedule / Make Safe Light Posts														
A1940	Dismantling & Removal of Balconies and Light Posts	6	12-Nov-20	19-Nov-20	1						Dismantling & Removal of Balconies and Light Posts														
A1960	Install Restored Balconies	12	26-May-21	11-Jun-21	29						Install Restored Balconies														
A1970	Install Restored Light Posts	2	26-May-21	27-May-21	39						Install Restored Light Posts														
WBS: Exterior Window Restoration		57	22-Dec-20	12-Mar-21	93																				
A2000	Abate Caulking -Exterior Windows	2	22-Dec-20	23-Dec-20	1						Abate Caulking -Exterior Windows														
A2010	Strip Paint -Exterior Windows	5	24-Dec-20	31-Dec-20	1						Strip Paint -Exterior Windows														
A2020	Recalk -Exterior Windows	5	12-Jan-21	18-Jan-21	117						Recalk -Exterior Windows														
A2030	Reglaze -Exterior Windows	5	22-Feb-21	26-Feb-21	93						Reglaze -Exterior Windows														
A2040	Repaint -Exterior Windows	5	01-Mar-21	05-Mar-21	93						Repaint -Exterior Windows														
A2240	Punchlist -Exterior Windows	5	08-Mar-21	12-Mar-21	93						Punchlist -Exterior Windows														
WBS: Interior Window Restoration		91	27-Oct-20	08-Mar-21	97																				
A2050	Schedule & Remove Shashes -Interior Windows	31	27-Oct-20	10-Dec-20	0						Schedule & Remove Shashes -Interior Windows														
A2060	Strip Paint & Repair -Interior Windows	5	11-Dec-20	17-Dec-20	0						Strip Paint & Repair -Interior Windows														
A2090	Repaint -Interior Windows	5	12-Jan-21	18-Jan-21	122						Repaint -Interior Windows														
A2080	Install Aluminum Frame Storm Windows -Interior Windows	5	16-Feb-21	22-Feb-21	97						Install Aluminum Frame Storm Windows -Interior Windows														
A2100	Reputty - Interior Windows	5	23-Feb-21	01-Mar-21	97						Reputty - Interior Windows														
A2250	Punchlist -Interior Windows	5	02-Mar-21	08-Mar-21	97						Punchlist -Interior Windows														
WBS: Interior		143	04-Jan-21	23-Jul-21	0																				
WBS: Phase 2 Interior		37	04-Jan-21	23-Feb-21	0																				
A1510	Make Safe -P2	3	04-Jan-21	06-Jan-21	0						Make Safe -P2														
A1520	Interior Demo -P2	3	07-Jan-21	11-Jan-21	0						Interior Demo -P2														
A1820	MEP Rough -P2	10	08-Jan-21	21-Jan-21	1						MEP Rough -P2														
A1530	Window Restoration -P2	15	12-Jan-21	01-Feb-21	0						Window Restoration -P2														
A1880	Rough Fire Alarm -P2	5	12-Jan-21	18-Jan-21	13						Rough Fire Alarm -P2														

Activity ID	Activity Name	Orig. Dur.	Early Start	Early Finish	Total Float	2021												2022								
						Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	
A1890	Fire Alarm Pre-Inspection -P2	2	19-Jan-21	20-Jan-21	13						█															
A1830	MEP Rough Inspection -P2	1	22-Jan-21	22-Jan-21	1																					
A1540	MEP Finishes -P2	5	25-Jan-21	29-Jan-21	1						█															
A1900	Fire Alarm Final Inspection -P2	5	25-Jan-21	29-Jan-21	11						█															
A1550	Interior Finishes -P2	8	02-Feb-21	11-Feb-21	0						█															
A1580	Phase 2 MEP Inspections	2	12-Feb-21	16-Feb-21	0						█															
A1560	Phase 2 Punchlist	5	17-Feb-21	23-Feb-21	0						█															
A1570	Phase 2 Complete	0		23-Feb-21	0						◆															
WBS: Phase 3 Interior		58	24-Feb-21	14-May-21	0																					
A1590	Make Safe -P3	5	24-Feb-21	02-Mar-21	0						█															
A1600	Interior Demo -P3	9	03-Mar-21	15-Mar-21	7						█															
A1610	Window Restoration -P3	20	03-Mar-21	30-Mar-21	28						█															
A1840	MEP Rough -P3	15	03-Mar-21	23-Mar-21	0						█															
A1850	MEP Rough Inspection -P3	1	24-Mar-21	24-Mar-21	0																					
A1620	MEP Finishes -P3	15	25-Mar-21	14-Apr-21	0						█															
A1630	Interior Finishes -P3	15	15-Apr-21	05-May-21	0						█															
A1660	Phase 3 MEP Inspections	2	06-May-21	07-May-21	0						█															
A1640	Phase 3 Punchlist	5	10-May-21	14-May-21	0						█															
A1650	Phase 3 Complete	0		14-May-21	0						◆															
WBS: Phase 4 Interior		48	17-May-21	23-Jul-21	0																					
A1670	Make Safe -P4	3	17-May-21	19-May-21	0						█															
A1680	Interior Demo -P4	3	20-May-21	24-May-21	0						█															
A1690	Window Restoration -P4	15	25-May-21	15-Jun-21	3						█															
A1910	Rough Fire Alarm -P4	5	25-May-21	01-Jun-21	0						█															
A1920	Fire Alarm Pre-Inspection -P2	2	02-Jun-21	03-Jun-21	0																					
A1860	MEP Rough -P4	10	04-Jun-21	17-Jun-21	0						█															
A1870	MEP Rough Inspection -P4	1	18-Jun-21	18-Jun-21	0																					
A1930	Fire Alarm Final Inspection -P2	5	18-Jun-21	24-Jun-21	15						█															
A1700	MEP Finishes -P4	10	21-Jun-21	02-Jul-21	0						█															
A1710	Interior Finishes -P4	8	06-Jul-21	15-Jul-21	0						█															
A1740	Phase 4 MEP Inspections	1	16-Jul-21	16-Jul-21	0																					
A1720	Phase 4 Punchlist	5	19-Jul-21	23-Jul-21	0						█															
A1730	Phase 4 Complete	0		23-Jul-21	0						◆															
WBS: Elevator		39	09-Mar-21	30-Apr-21	58																					
A1750	Elevator Modernization	30	09-Mar-21	19-Apr-21	58						█															
A1760	Elevator Inspection	9	20-Apr-21	30-Apr-21	58						█															
WBS: Stairwell Work		50	02-Feb-21	12-Apr-21	72																					
A1770	Stairwell Work	50	02-Feb-21	12-Apr-21	72						█															
WBS: Site		5	26-Jul-21	30-Jul-21	0																					
A1070	Clean-Up & Demobilization	5	26-Jul-21	30-Jul-21	0																			█		
