




1 FIRST FLOOR PLAN
1/16" = 1'-0"

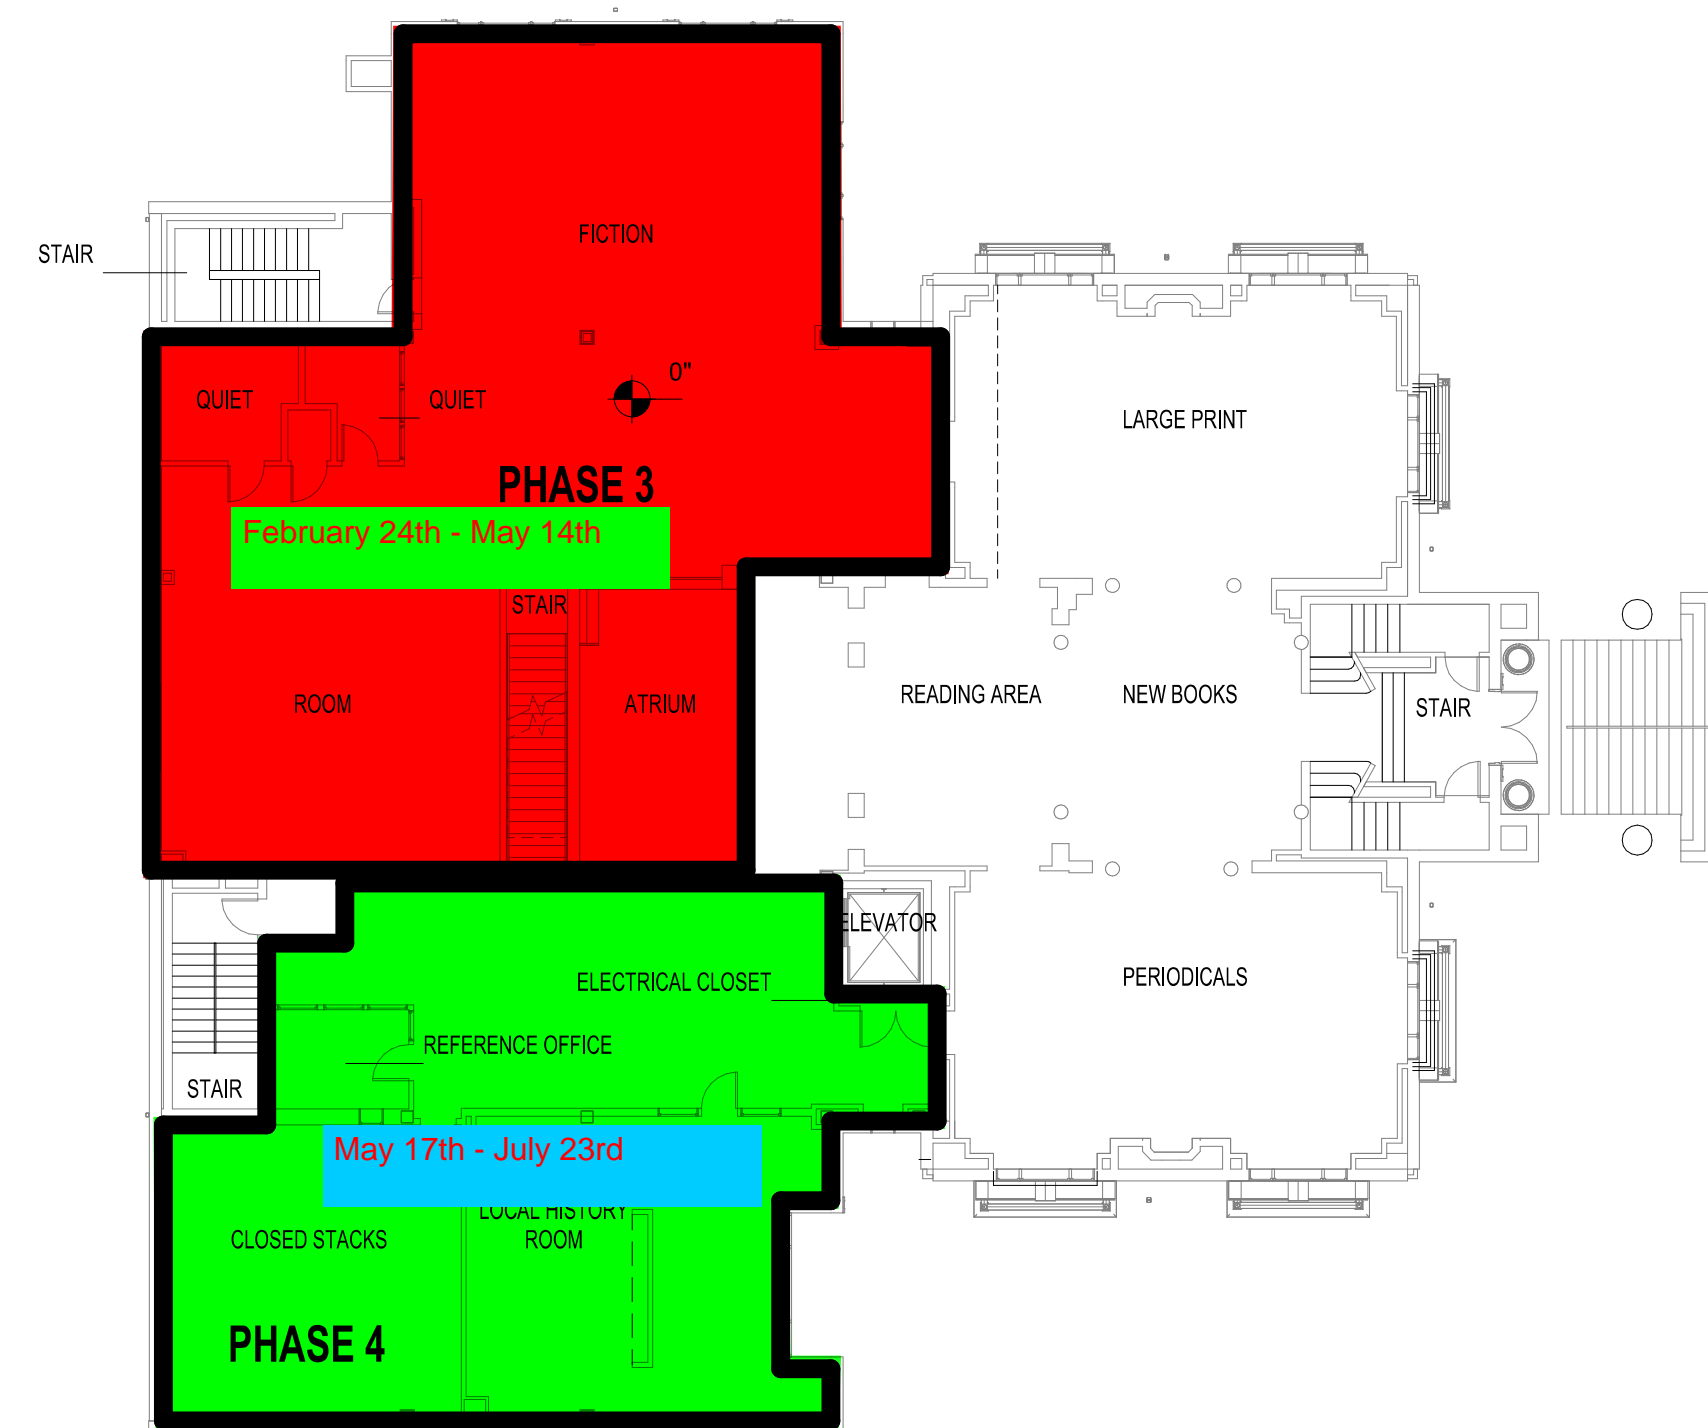


2 SECOND FLOOR PLAN
1/16" = 1'-0"

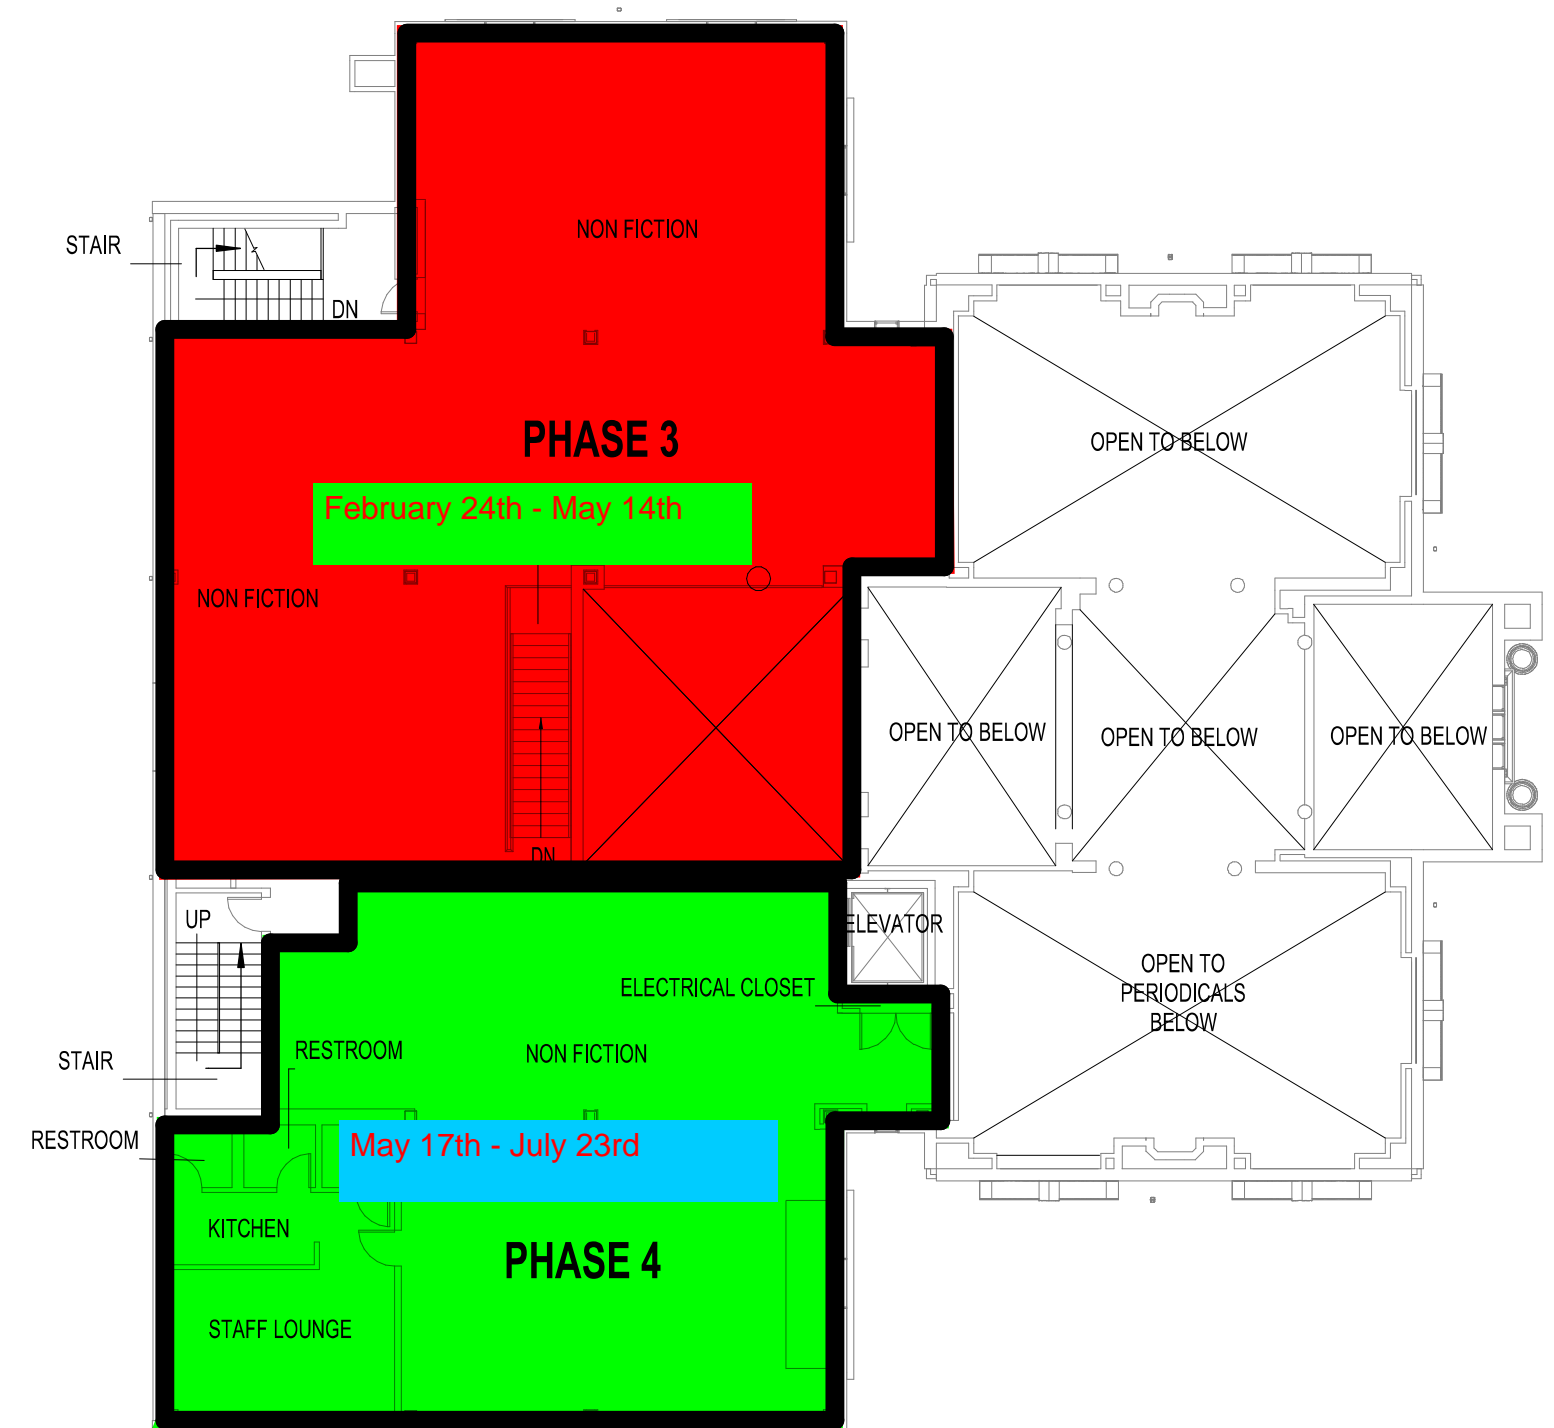

3 THIRD FLOOR PLAN
1/16" = 1'-0"

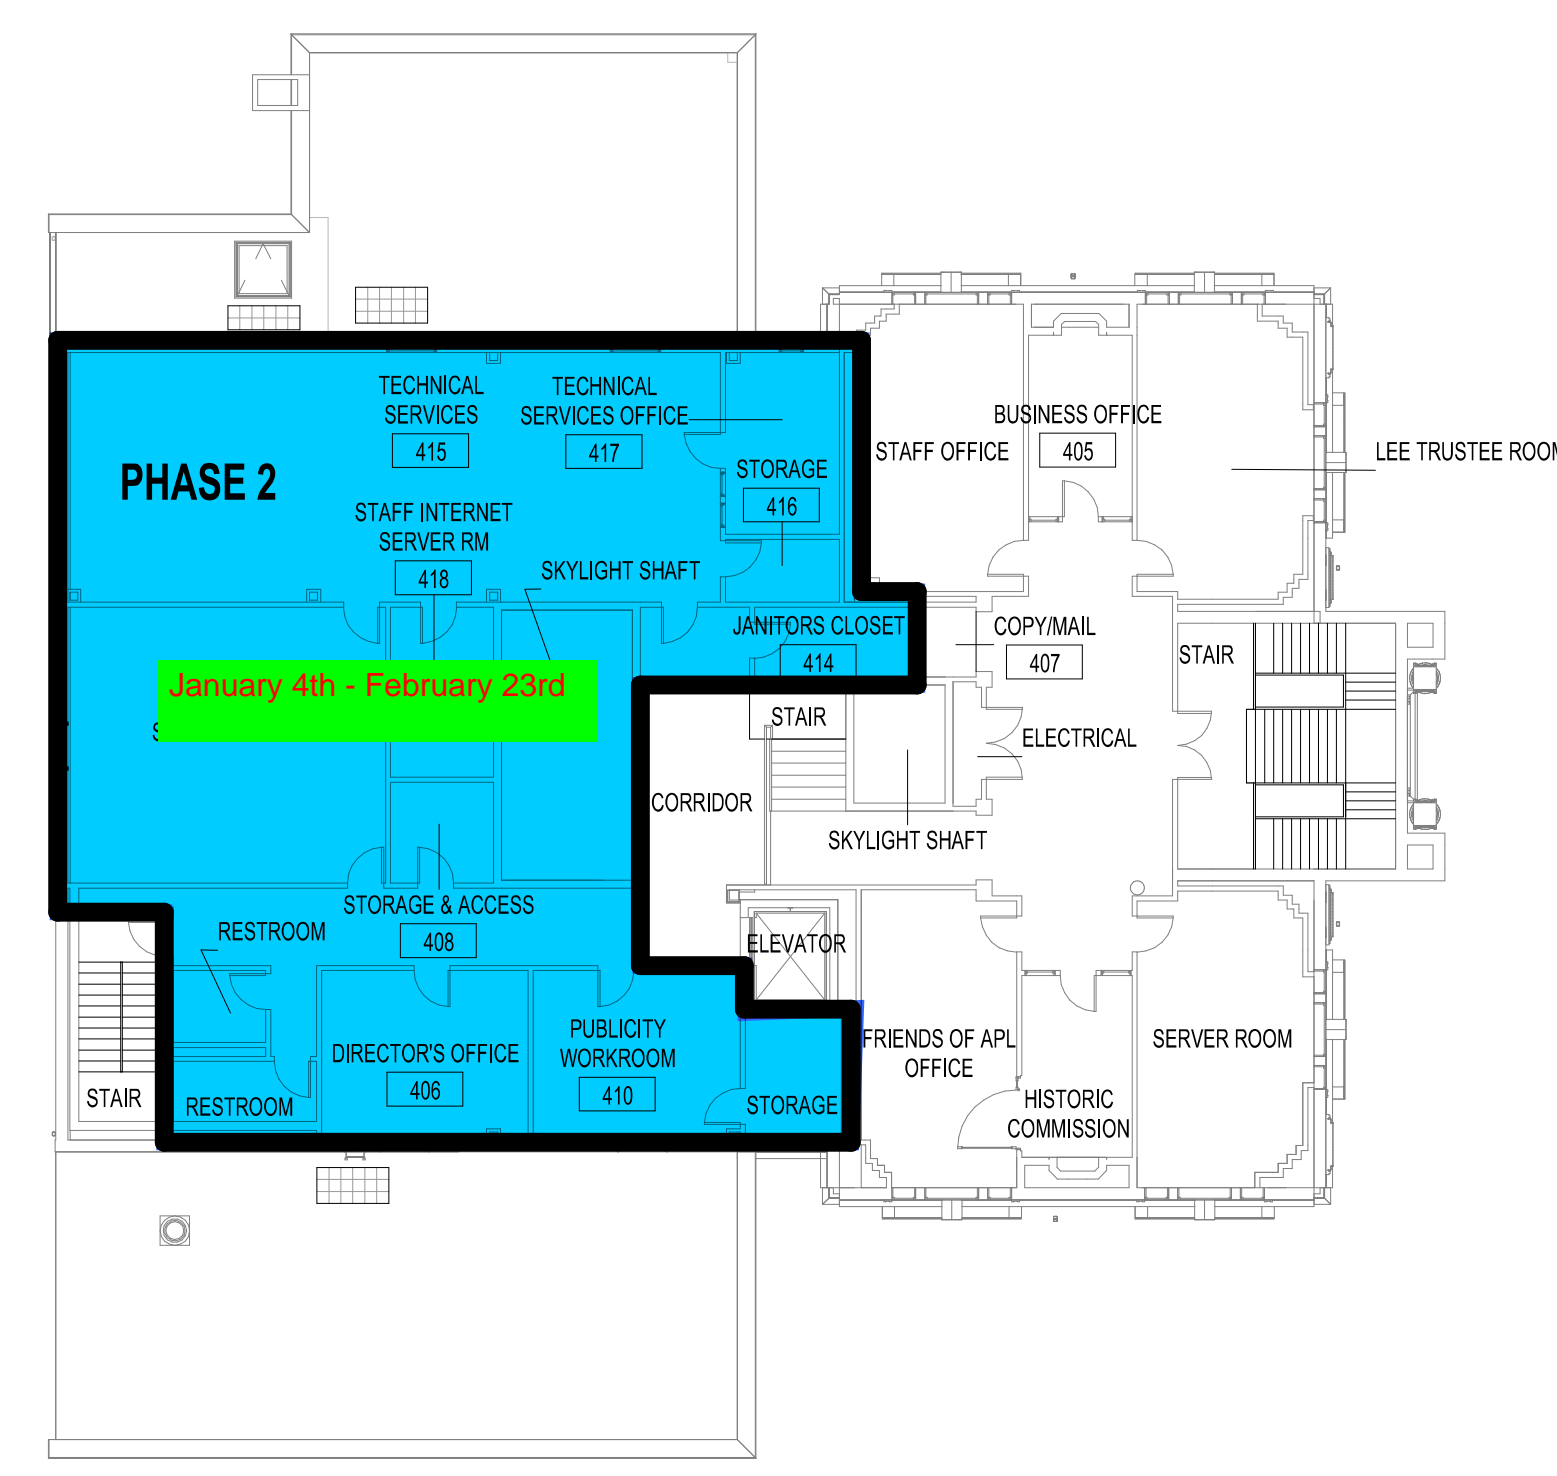

4 FOURTH FLOOR PLAN
1/16" = 1'-0"

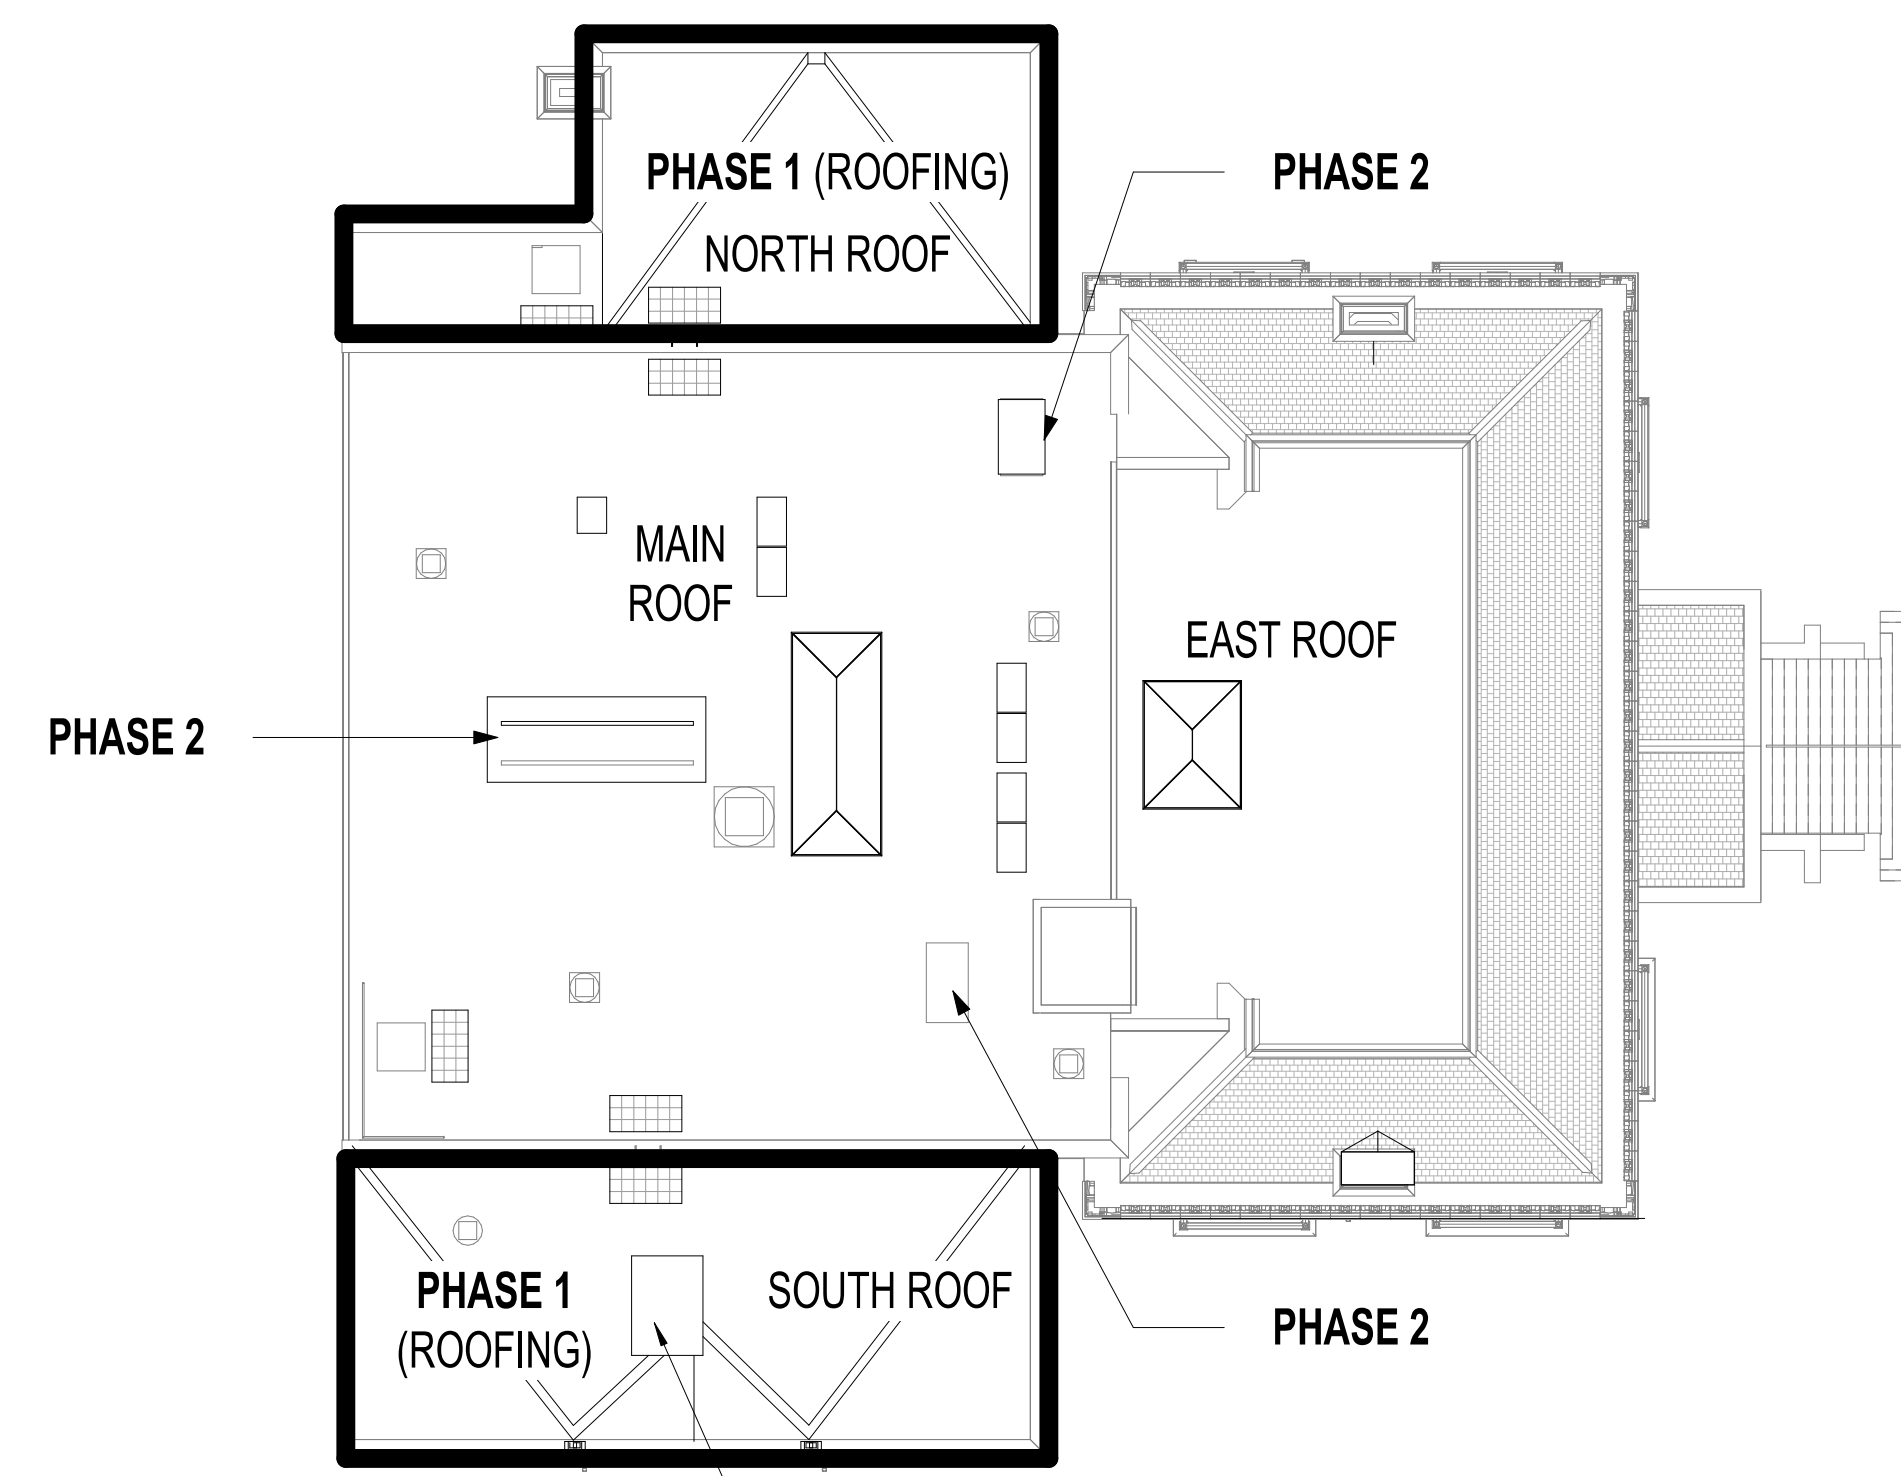

5 ROOF PLAN
1/16" = 1'-0"

GENERAL NOTES PHASING PLANS


- 100. THE LIBRARY WILL BE OCCUPIED DURING CONSTRUCTION. THESE PLANS SHOW PHASING THAT WILL ALLOW SOME AREAS TO BE DEDICATED FULLY TO THE CONTRACTOR FOR A DURATION OF TIME, SPECIFICALLY FOR MECHANICAL WORK. THE CONTRACTOR IS TO PROVIDE A WORK PLAN TO SHOW HOW THE WORK WILL BE PHASED, INCLUDING ALL TRADES FOR THE FULL PROJECT.
- 101. EXISTING HEATING/COOLING AND VENTILATION ARE TO BE MAINTAINED THROUGHOUT THE BUILDING, DISCONNECTED ONLY AT EACH PHASE AS NEW EQUIPMENT IS CONNECTED. SOME AREAS WITH MINIMAL WORK ARE NOT SHOWN AS PART OF A PHASED CONTRACTOR AREA. THOSE ITEMS ARE TO BE DONE WITH THE RELATED PHASE, BUT SCHEDULED TO ALLOW FOR ONE-DAY ACCESS.
- 102. LIBRARY SHELVING, BOOKS, AND OTHER FIXED ITEMS WILL REMAIN IN PLACE. THE CONTRACTOR IS RESPONSIBLE FOR PROVIDING A PROTECTION PLAN AND PROTECTING THESE ITEMS FROM CONSTRUCTION ACTIVITY. INCLUDE BARRIERS AT THE BOUNDARIES OF WORK AREAS TO CLOSE OFF FROM THE PUBLIC AND STAFF. THE OWNER WILL REMOVE COMPUTERS AND OTHER LOOSE EQUIPMENT FROM SPACES WHERE THE CONTRACTOR WILL WORK.
- 103. CIRCULATION ROUTES AND EGRESS MUST BE MAINTAINED FOR THE STAFF AND PUBLIC. WORK AT AREAS THAT ARE NOT PART OF CONTRACTOR ENCLOSURE ARE TO BE SCHEDULED FOR WHEN THE LIBRARY IS CLOSED.
- 104. ACCESS FOR PATRONS AT THE MAIN ENTRY, CIRCULATION DESK AND ELEVATOR IS TO BE MAINTAINED AT ALL PHASES.
- 105. THE MAIN ROOF AREA IS AVAILABLE TO THE CONTRACTOR DURING ALL PHASES. ROOF PHASE 1 WORK REFLECTS THE REQUIREMENT TO DO THAT ROOFING WORK FIRST. REPAIR WORK AT THE MAIN ROOF IS TO BE COORDINATED WITH THE REMOVAL OF EXISTING EQUIPMENT AND INSTALLATION OF NEW EQUIPMENT. NEW EQUIPMENT MAY BE STORED ON THE ROOF IN ADVANCE OF CONNECTION, AS LONG AS SATISFACTORY PROTECTION IS PROVIDED.
- 106. THE EAST ROOF, EXTERIOR ELEVATION, AND WINDOW WORK IS NOT SHOWN TO BE PART OF ANY PHASE. THE CONTRACTOR IS TO INCLUDE THESE AREAS IN THE OVERALL SCHEDULED WORK PLAN. WINDOW WORK DEPENDS ON SCOPE, BUT IT IS ASSUMED THAT ACCESS TO THE INTERIOR WILL BE GIVEN, IN A MANNER THAT ALLOWS ACCESS JUST TO THE WINDOWS, WITH ROOMS CLOSED TO THE PUBLIC/STAFF FOR INDIVIDUAL DAYS. ROOMS WILL NOT HAVE CONTENTS REMOVED FOR THIS WORK. THE ELEVATOR IS NOT PART OF ANY CONTRACTOR WORK AREA PHASE. THE ELEVATOR IS FOR LIBRARY USE ONLY, UNLESS SPECIFIC PERMISSION IS GIVEN. THE CONTRACTOR IS TO PLAN ON USING STAIRS FOR ACCESS. ANY USE OF STAIRS OR ELEVATOR FOR MATERIALS REQUIRES PROTECTION TO BE PROVIDED.

REFERENCE NOTES PHASING PLANS

PP1 THIS ROOM CONTAINS THE LIBRARY'S NETWORKING EQUIPMENT AND INCOMING INTERNET SERVICE. THE OWNER WILL NEED TO HAVE ACCESS TO THE SPACE THROUGHOUT THE PROJECT, INCLUDING DURING PHASE 2. THE CONTRACTOR IS TO ALLOW THE OWNER TO ACCESS THIS ROOM AS REQUESTED FOR THE DURATION OF PHASE 2 WORK.

LEGEND

█ = CONTRACTOR WORK AREA



ARCHITECT
bh+a
 Bargmann Hendrie + Archetype, Inc.
 9 Channel Center Street
 Boston, MA 02210
 617 350-0450 Tel

PROJECT NAME
Attleboro Public Library Building Envelope Repair & Mechanical System Upgrade

74 North Main Street,
 Attleboro, MA 02703

CLIENT
City of Attleboro

Capital Projects Office, 2nd Floor
 77 Park Street, Attleboro, MA 02703

PROJECT TEAM

MEP ENGINEER
 Allied Consulting Engineering
 235 Littleton Road, Suite 5
 Westford, MA 01886

STRUCTURAL ENGINEER
 Foley Buft Roberts & Associates, Inc.
 2150 Washington Street
 Newton, MA 02462
 617.527.9500

ELEVATOR CONSULTANT
 B SQUARED ENGINEERING
 159 Mill Brook Road
 Stamford, CT 06902
 203.989.9029

REVISIONS

1	
2	
3	
4	
5	DATE

DRAWING TITLE
PHASING PLANS

DRAWING INFORMATION

July 31, 2020	DATE OF ISSUE
100% Construction Documents	DESCRIPTION
1/16" = 1'-0"	SCALE
Author	DRAWN BY
3382_02	PROJECT #
[File Location.rvt]	FILE NAME

DRAWING NUMBER

G002
